



## GREENWOODS CORNER SAFETY IMPROVEMENTS

The Greenwood's Corner Signalised Crossing project is planned to commence on 30 March 2025 (pending TMP approval). Below is the indicative staging plan for this work. AT will reconfirm these once all approvals are obtained.

The project will be delivered in five stages and will be done during the night to minimize disruption to public around the shops. Our program is for 25 to 30-night shift, and the occasional off-peak hours dayworks.

Night works will be between 7PM and 5 AM. Traffic Lane closures will be in place during night works. There will be no lane closures during the day.

When required, the occasional day works will be between 10 AM and 3PM. Lane closures will be in place during the day work hours and lanes will be functioning as usual during peak hours.


Pedestrian access and access to shops will be maintained throughout the work period.

Cones and signs will be moved to the edge pavement when the site is unattended for safety reasons. No impact on traffic and parking due to these cones

AT and their contractor will aim to avoid daytime work during Easter week, subject to unforeseen delays.

Any concerns about the project, contact us - [projects@at.govt.nz](mailto:projects@at.govt.nz) or call 09 930 5090.

For queries related to construction, Contact Ikram, Construction Manager, Traffica Limited [ikram@traffica.co.nz](mailto:ikram@traffica.co.nz) – 021 638 728

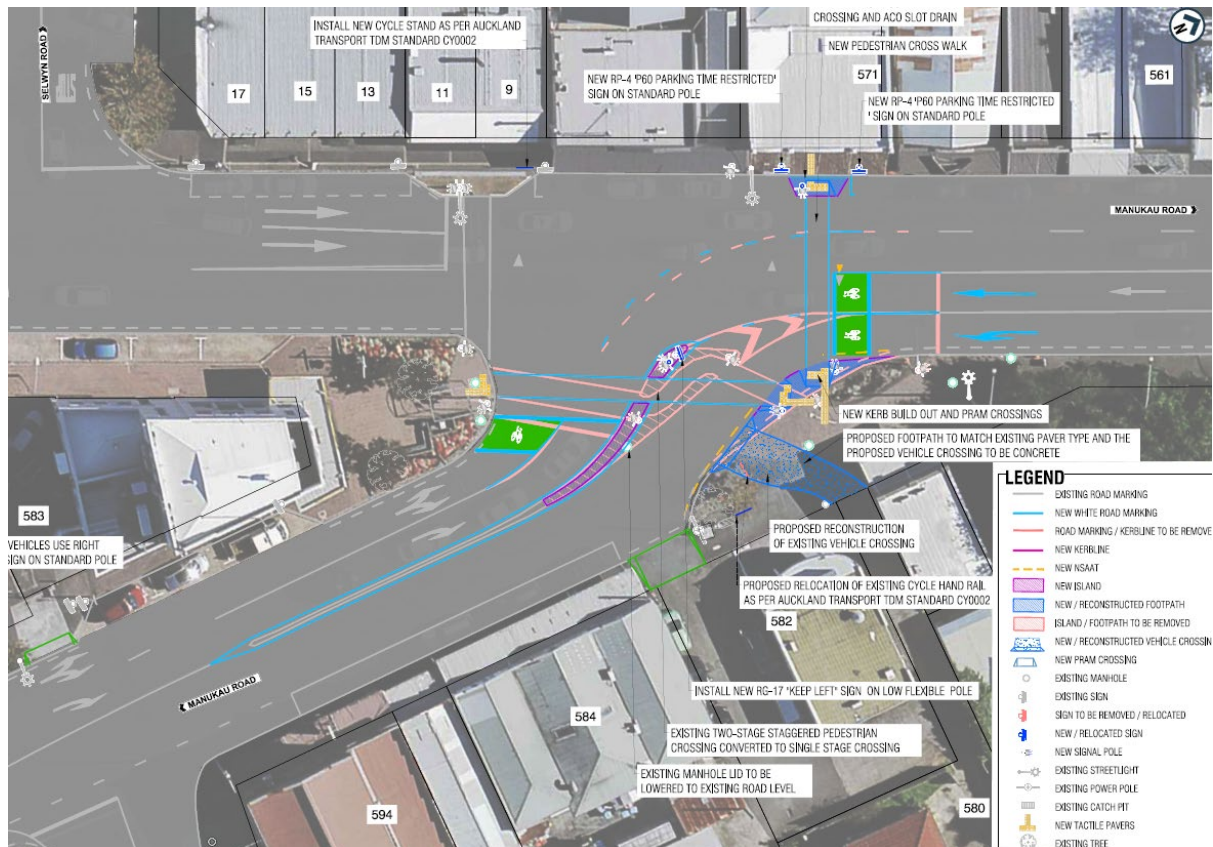

Stage 1 –



2-3 nights (occasional day work may be needed)

Install ducting across Manukau Rd, install tactile pavers and pram crossing

1 northbound lane closed during works.

No impact on car parking spaces in Stage 1

Stage 2



6-8 nights (occasional day work required)

Install ducting across Manukau Rd, remove existing traffic islands. Install new traffic islands and signal infrastructure.

1 northbound lane closed during works.

No impact on car parking spaces in Stage 2

Stage 3



8-10 nights (Occasional daytime work may be required)

Install ducting across Manukau Rd, Install new kerb and channel, footpath, pram crossing.  
Install new traffic islands and signal Infrastructure.

1 southbound lane closed during works.

No impact on car parking spaces in Stage 3

## Stage 4



4 Night shifts primarily from Sunday to Thursday, with occasional work on other nights.

Install ducting across Manukau Road

Stop/Go Closures will impact both southbound and northbound lanes.

Please note that car parking will be affected, and only a limited number of spaces will be available.

Delivery vehicles will have access to the businesses.

Stage 5



5 nights (occasional daytime work may be required)

Install new kerb buildout, footpath, pram crossing. Install new traffic islands and signal infrastructure.

No impact on traffic lanes

Car parking will be affected—fewer spaces will be available.
